

# RESERVOIRS 1 AND 2 PUMP STATION UPGRADES PROJECT

April 23, 2025

## Reservoir 1 – Site Layout

1. Dewatering Pit
2. Heavy Equipment Port
3. Chemical Management
4. Generators



## Reservoir 1 – Dewatering Pit



3 | April 23, 2025



## Reservoir 1 Heavy Equipment Port Foundation




4 | April 23, 2025





## Reservoir 1 – Chemical Facility Concrete Pads

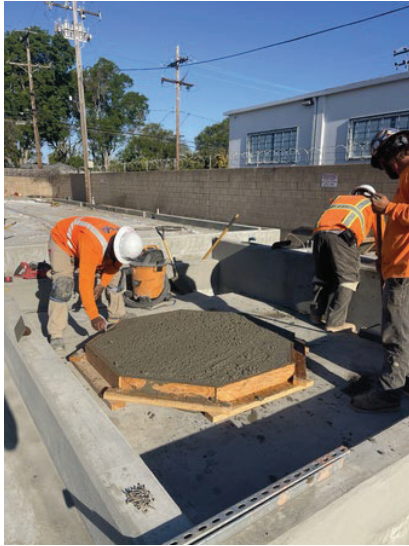

5 | April 23, 2025



## Reservoir 1 – Generator Forms




6 | April 23, 2025





## Reservoir 2 – Site Layout

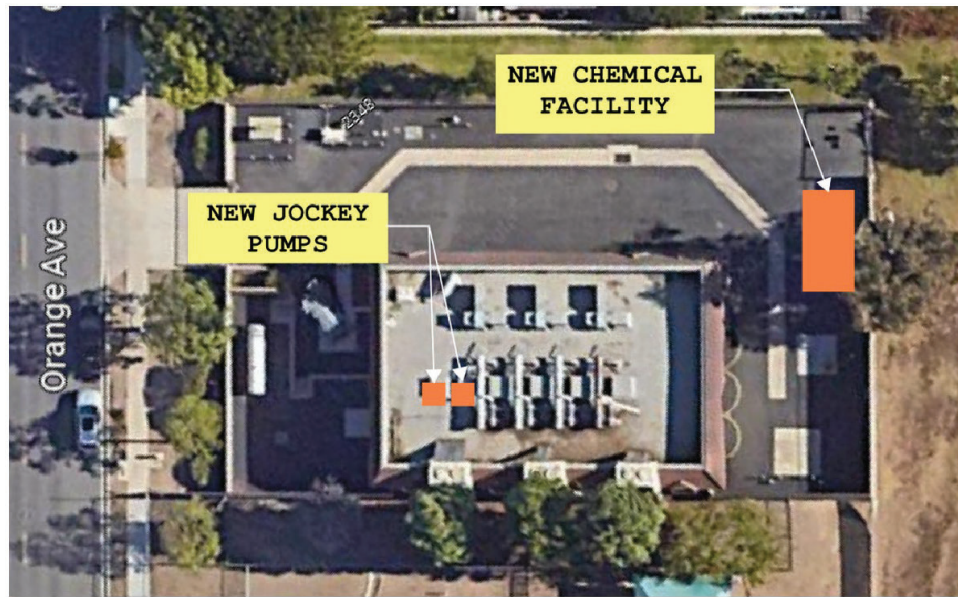

7 | April 23, 2025



## Reservoir 2 Chemical System Pad and Panels



8 | April 23, 2025



## Variable Frequency Drives Delivered!



9 | April 23, 2025



## Reservoir Project Schedule


Calendar Year	2024				2025				2026	
Task	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Submittals and Procurement										
Reservoir 2										
Reservoir 1										
Project Closeout										

10 | April 23, 2025





# Reservoir Project Planned vs. Actual

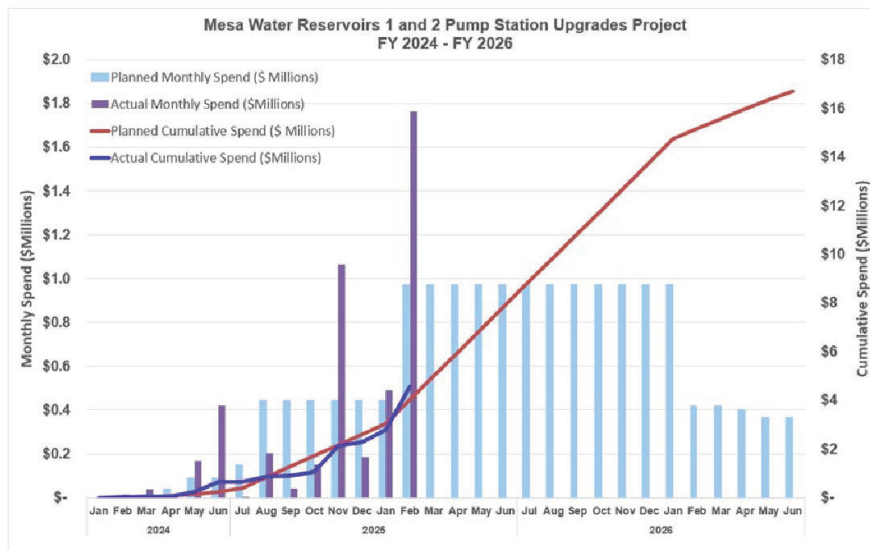

11 | April 23, 2025



# QUESTIONS?
